

I NEED TO DELETE THIS COLUMN
AND JUST MAKE 1 COLUMN


ROOM FINISH SCHEDULE																												
NO	NAME	FLOOR		BASE	WALLS																CLG	CLG HGT	REMARKS					
		VINYL TILE	CERAMIC TILE 1	CERAMIC TILE 2	VINYL	CERAMIC TILE BASE 1	CERAMIC TILE BASE 2	NORTH				SOUTH				EAST				WEST				SUSPENDED ACCOUSTICAL	NO CEILING	8'	9'	
								PAINTED GYPSUM BOARD	48" AFF CERAMIC TILE	96" AFF CERAMIC TILE	EPOXY PAINT	CERAMIC CHAIR RAIL	PAINTED GYPSUM BOARD	48" AFF CERAMIC TILE	96" AFF CERAMIC TILE	EPOXY PAINT	CERAMIC CHAIR RAIL	PAINTED GYPSUM BOARD	48" AFF CERAMIC TILE	96" AFF CERAMIC TILE	EPOXY PAINT	CERAMIC CHAIR RAIL						
101	WAITING	0	0		0	0		0			0			0			0			0		0	0	0	0			
102	RECEPTIONIST	0						0			0			0					0		0	0	0	0	0			
103	CLOSET	0			0			0			0			0					0		0	0	0	0	0			
104	OFFICE MANAGER	0			0			0			0			0					0		0	0	0	0	0			
105	RESTROOM	0			0			0			0			0					0		0	0	0	0	0			
106	RESTROOM	0			0			0			0			0					0		0	0	0	0	0			
107	EXAM 1	0			0			0			0			0					0		0	0	0	0	0			
108	HALLWAY	0			0			0			0			0					0		0	0	0	0	0			

ROOM FINISH SCHEDULE																																	
NO	NAME	FLOOR	BASE	WALLS																CLG	CLG HGT	REMARKS											
				NORTH				SOUTH				EAST				WEST																	
				VINYL TILE	CERAMIC TILE 1	CERAMIC TILE 2	VINYL	CERAMIC TILE BASE 1	CERAMIC TILE BASE 2	PAINTED GYPSUM BOARD	48" AFF CERAMIC TILE	96" AFF CERAMIC TILE	EPOXY PAINT	CERAMIC CHAIR RAIL	PAINTED GYPSUM BOARD	48" AFF CERAMIC TILE	96" AFF CERAMIC TILE	EPOXY PAINT	CERAMIC CHAIR RAIL				PAINTED GYPSUM BOARD	48" AFF CERAMIC TILE	96" AFF CERAMIC TILE	EPOXY PAINT	CERAMIC CHAIR RAIL						
109	EXAM 2	0					0					0						0					0										
110	DOCTORS OFFICE	0					0					0						0					0										
111	LAB	0					0					0						0					0										
112	PROCEDURE	0					0					0						0					0										
113	CLOSET	0					0					0						0					0										
114	BREAKROOM	0					0					0						0					0										
115	CLOSET	0					0					0						0					0										


DOOR SCHEDULE							
NO.	WIDTH	HEIGHT	THICKNESS	DESCRIPTION	DET.	TYPE	FRAME
1	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
2	3' - 0"	6' - 8"	2"	BI-FOLD SOLID CORE WITH METAL FRAME	4	B	METAL
3	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
4	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
5	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
6	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
7	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
8	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL

DOOR SCHEDULE							
NO.	WIDTH	HEIGHT	THICKNESS	DESCRIPTION	DET.	TYPE	FRAME
9	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
10	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
11	3' - 0"	6' - 8"	2"	BI-FOLD SOLID CORE WITH METAL FRAME	4	B	METAL
12	6' - 0"	6' - 8"	2"	BI-FOLD SOLID CORE WITH METAL FRAME	3	C	METAL
13	8' - 8"	6' - 8"	2"	ROLLING GARAGE DOOR			METAL
14	3' - 0"	6' - 8"	2"	INTERIOR SOLID CORE WOOD DOOR WITH METAL FRAME	1	A	METAL
15	3' - 1"	8' - 0"	2"	GLASS			METAL


Window Schedule				
Type Mark	Width	Height	Model	Comments
A	3' - 0"	4' - 0"		

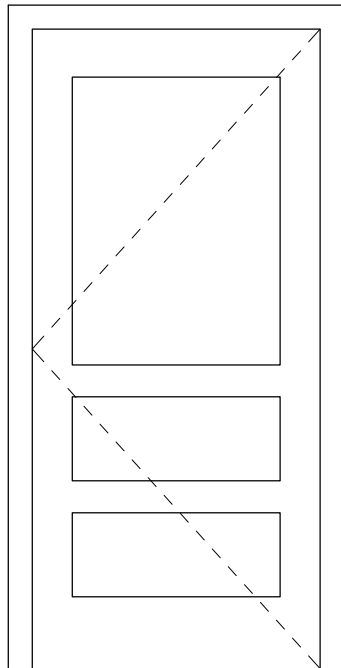


TYPE A
INTERIOR SOLID WOOD
CORE WITH METAL FRAME

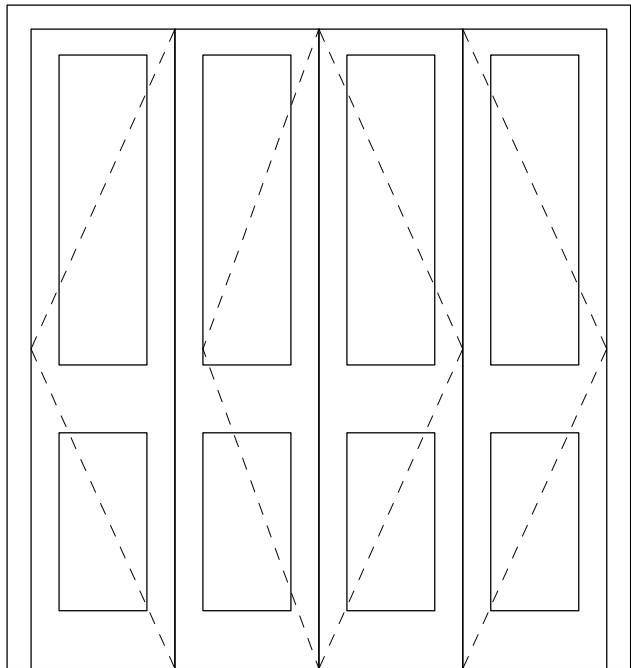

TYPE B
4 PANEL BI-FOLD INTERIOR SOLID WOOD
CORE WITH METAL FRAME

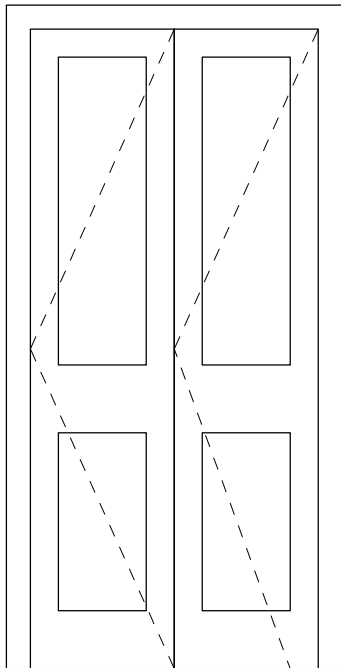

TYPE C
2 PANEL BIFOLD INTERIOR
SOLID WOOD CORE WITH
METAL FRAME



TYPE A
FIXED WINDOW WITH
METAL FRAME

DOOR TYPES

WINDOW TYPES

SCHEDULES

SCALE: 1/2" = 1'-0"

#	REVISIONS	DATE	BY

BUMPUS AND ASSOCIATES, INC.
ARCHITECTURE - INTERIOR DESIGN
www.BUMPUSANDASSOCIATES.com
603 FRONT STREET
CELEBRATION, FLORIDA 34747
AA 000261

PH (407) 564-0200
FX (407) 564-0223
AR 000845

Approved By:

Daniel L. Bumpus
AR 0008045
Date

STEVEN'S PLANTATION
DOCTOR'S OFFICE
3131 INNOVATION DR
ST. CLOUD, FLORIDA

DRWN: Author
APVD: Approve

DATE:
APRIL 4TH, 2011

SCALE:
AS SHOWN

JOB NUMBER:
11111

SHEET:
A2.2
